



# FIRE STATION #3 PROJECT

## REPORT #1: JANUARY 2018

### Contents

1. Project Summary
2. Project Activities
3. Photos



### MONTHLY PROGRESS REPORT

### Project Team

#### City of Palo Alto

Matt Raschke  
Young Tran  
Bridgette Medved-Perez

#### Shah Kawasaki Architects

Chenglong Tsai  
Olivia Asuncion

#### Nova Partners, Inc.

Hans de Roos  
Frank Arsenault

#### Strawn Construction

Tim Foster  
Max Munoz  
Bob Cardwell

# Fire Station #3 Replacement Project

## January 2018

### MONTHLY REPORT

#### **Project Summary**

Fire Station #3 was originally constructed in 1948 as a wood-framed structure located on the northwest corner of Newell Road and Embarcadero Road (799 Embarcadero Road) in Palo Alto, CA. The existing Fire Station will be demolished and replaced with a new, ground-up 6,663 SF two-story Fire Station meeting the requirements of the Essential Services Buildings Seismic Safety Act (ESBSSA; 1986). Shah Kawasaki Architects of Oakland provided the architectural and engineering design for the project which was approved by the City of Palo Alto Architectural Review Board on March 2, 2017.

The construction phase of the project began with bidding and subsequent City Council approval of the construction contract on November 13, 2017. The work will be performed by Strawn Construction. The contract was signed and executed on December 21, 2017. Construction began on January 8, 2018. The project is scheduled to be completed in January 2019. Below is a summary of the activities completed in January 2018 and upcoming activities for February 2018.

#### **January 2018 Activities**

Strawn Construction mobilized to the site on January 8, 2018. The following activities were completed this month:

- Site fencing was erected along the perimeter of the site.
- Tree protection has been installed per the plans approved by David Babby, the project Arborist.
- Abatement began on January 15, 2018 and was completed on January 23, 2018.
- Official abatement clearance was granted by Patriot Laboratories, on January 26, 2018.
- Demolition crews mobilized on January 29, 2018.

- A ground-breaking ceremony attended by Mayor Liz Kniss, Councilmember Greg Scharff, Councilmember Lydia Kou, City Manager James Keene, Fire Chief Eric Nickel, members of the Fire Department and Public Works Engineering was held on January 30, 2018.
- Demolition of the existing structures was completed on January 31, 2018.

### **Upcoming Activities**

During February 2018, Strawn Construction expects to perform the following activities:


- Demolition of the existing building concrete foundations and slab on grade.
- Demolition of the existing site utilities in preparation for new utility connections.
- Site grading, and removal of site hardscape will be completed.
- Survey and layout of new building pad and all underground utilities.
- Excavation and compaction for the building pad subgrade.
- Trenching and installation for the water, sanitary sewer, and storm water utilities.

January 2018

## Construction Photos



Ground-breaking Ceremony.

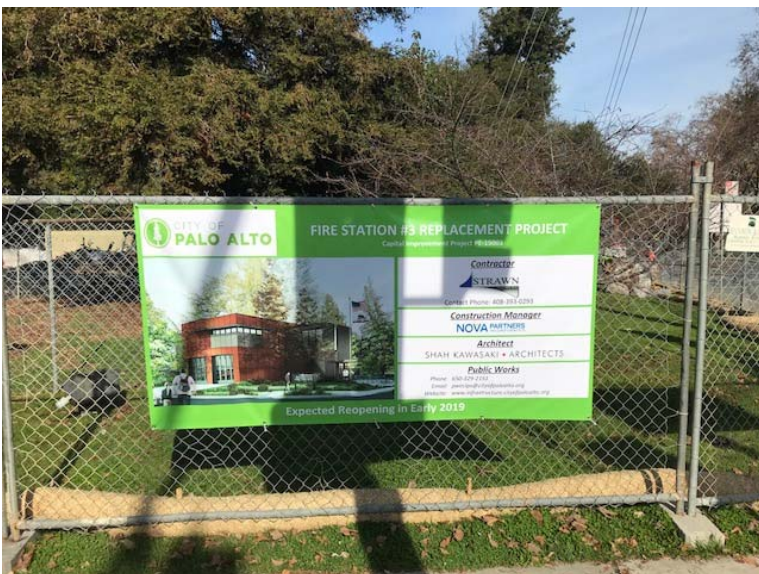

Site sign installed on site fence.

January 2018

## Construction Photos



Demolition of existing structure.



Existing structure demo completed.
