



FIRE STATION #3 PROJECT

REPORT #11: NOVEMBER 2018

Contents

- 1. Project Summary
- 2. Project Activities
- 3. Photos



MONTHLY PROGRESS REPORT

Project Team

City of Palo Alto

Matt Raschke
Young Tran
Bridgette Medved-Perez

Shah Kawasaki Architects

Chenglong Tsai
Olivia Asuncion

Nova Partners, Inc.

Hans de Roos
Frank Arsenault
Jason Luong

Strawn Construction

Max Munoz
Billie Harris
Jake Strawn
Randy Strawn
Donnie Durham
Don Teixeira

Fire Station #3 Replacement Project

November 2018

MONTHLY REPORT

Project Summary

Fire Station #3 was originally constructed in 1948 as a wood-framed structure located on the northwest corner of Newell Road and Embarcadero Road (799 Embarcadero Road) in Palo Alto, CA. The existing Fire Station will be demolished and replaced with a new, ground-up 6,663 SF two-story Fire Station meeting the requirements of the Essential Services Buildings Seismic Safety Act (ESBSSA; 1986). Shah Kawasaki Architects of Oakland provided the architectural and engineering design for the project which was approved by the City of Palo Alto Architectural Review Board on March 2, 2017.

The construction phase of the project began with bidding and subsequent City Council approval of the construction contract on November 13, 2017. The work will be performed by Strawn Construction via the contract signed and executed on December 21, 2017. Construction began on January 8, 2018.

November 2018 Activities

Strawn Construction continued construction activities in November 2018 with the following activities completed this month:

- Continued protection of the new slab using mirafi and OSB.
- M-E-P rough-in continued.
- Sprinkler rough-in continued.
- Underground utilities installed water and gas lines onto the project site.
- CMU wall foundation was placed.
- Trash enclosure slab was placed.
- CMU block wall install was started.
- Exterior waterproofing started.
- Roofing install started.
- Continued tree protection maintenance and watering of existing trees.

Upcoming Activities

During December 2018 – January 2019, Strawn Construction expects to perform the following activities:


- M-E-P rough-in will finish.
- Fire sprinkler rough-in will be completed. Flush the fire water main.
- CMU block wall will be completed.
- Install of the building envelope waterproofing will finish.
- Roofing install will complete.
- Install of metal railing guardrails.
- Underground utilities will continue.
- Grading for the new retention basins.
- Managing tree protection and watering as needed.
- SWPPP management will continue during the fall and winter seasons.

November 2018

Construction Photos



Trash enclosure slab prepped for pour.

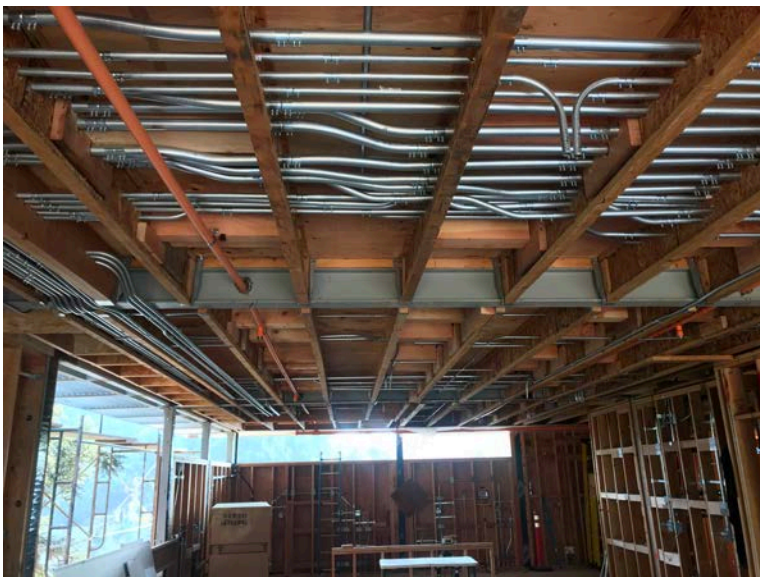

Interior MEP rough in on 2nd floor.

November 2018

Construction Photos



Trash enclosure slab pour.



CMU wall foundation pour.

November 2018

Construction Photos



CMU wall block install.



Building envelope waterproofing install.

November 2018

Construction Photos



Roofing install.
